Woodfield Farmington Phase II
Charlotte, NC

Exhibit E - Preliminary Construction Schedule

ID	Task Name	Duration
1	**Farmington II, Charlotte NC**	**697 days**
2	**Notice To Proceed**	**0 days**
3	**Project Critical Milestones**	**499 days**
4	**Owner Deliverable Milestones**	**409 days**
5	Builders Risk Policy In Place	0 days
6	**Permits**	**35 days**
7	Land Disturbance Permits Issued	0 days
8	Grading Permit Issued	0 days
9	Foundation/Building Permits Issued	0 days
10	**Shop Drawing Approvals**	**6 days**
11	Erosion Storm Structure Shop Drawing Approvals	0 days
12	Precast Structures Shop Drawing Approvals	0 days
13	**Utilities**	**393 days**
14	Utility Permit to Construct Issued	0 days
15	For Construction Power Plan	0 days
16	For Construction Telecom/Internet Plan	0 days
17	Active Temp Construction Power	0 days
18	Active Construction Water	0 days
19	House/Unit Electrical Service Applications	0 days
20	**Electric Meters Set**	**93 days**
21	Building 3	0 days
22	Building 2	0 days
23	Building 4	0 days
24	Building 1	0 days
25	Water/Sewer Permit to Operate Issued	0 days
26	Water Meters Set	0 days
27	Active Phone Lines	0 days
28	**Binder Course for Framing**	0 days
29	**Turnover**	**91 days**
30	Clubhouse	0 days
31	Building 3	0 days
32	Building 2	0 days
33	Building 4	0 days
34	Building 1	0 days
35	**Project Completion**	0 days
36	**Site Construction (# Of Acres)**	**468 days**
37	**Initial Sitework**	**148 days**
38	**Erosion Control PH1 (B4-B3-B2)**	**10 days**
39	**Erosion Control PH1 (B1)**	**5 days**
40	**Export SP1**	**20 days**
41	**Mass Grading**	**25 days**
42	**Rock Blasting**	1 day
43	**Building Pad Grading**	**23 days**
49	**Utilities**	**74 days**
50	**Sanitary Sewer**	**17 days**
55	**Storm**	**24 days**
67	**Rough Grade Roadways**	**20 days**
72	**Curb/Gutter**	**20 days**
77	**Domestic/Fire Water**	**25 days**

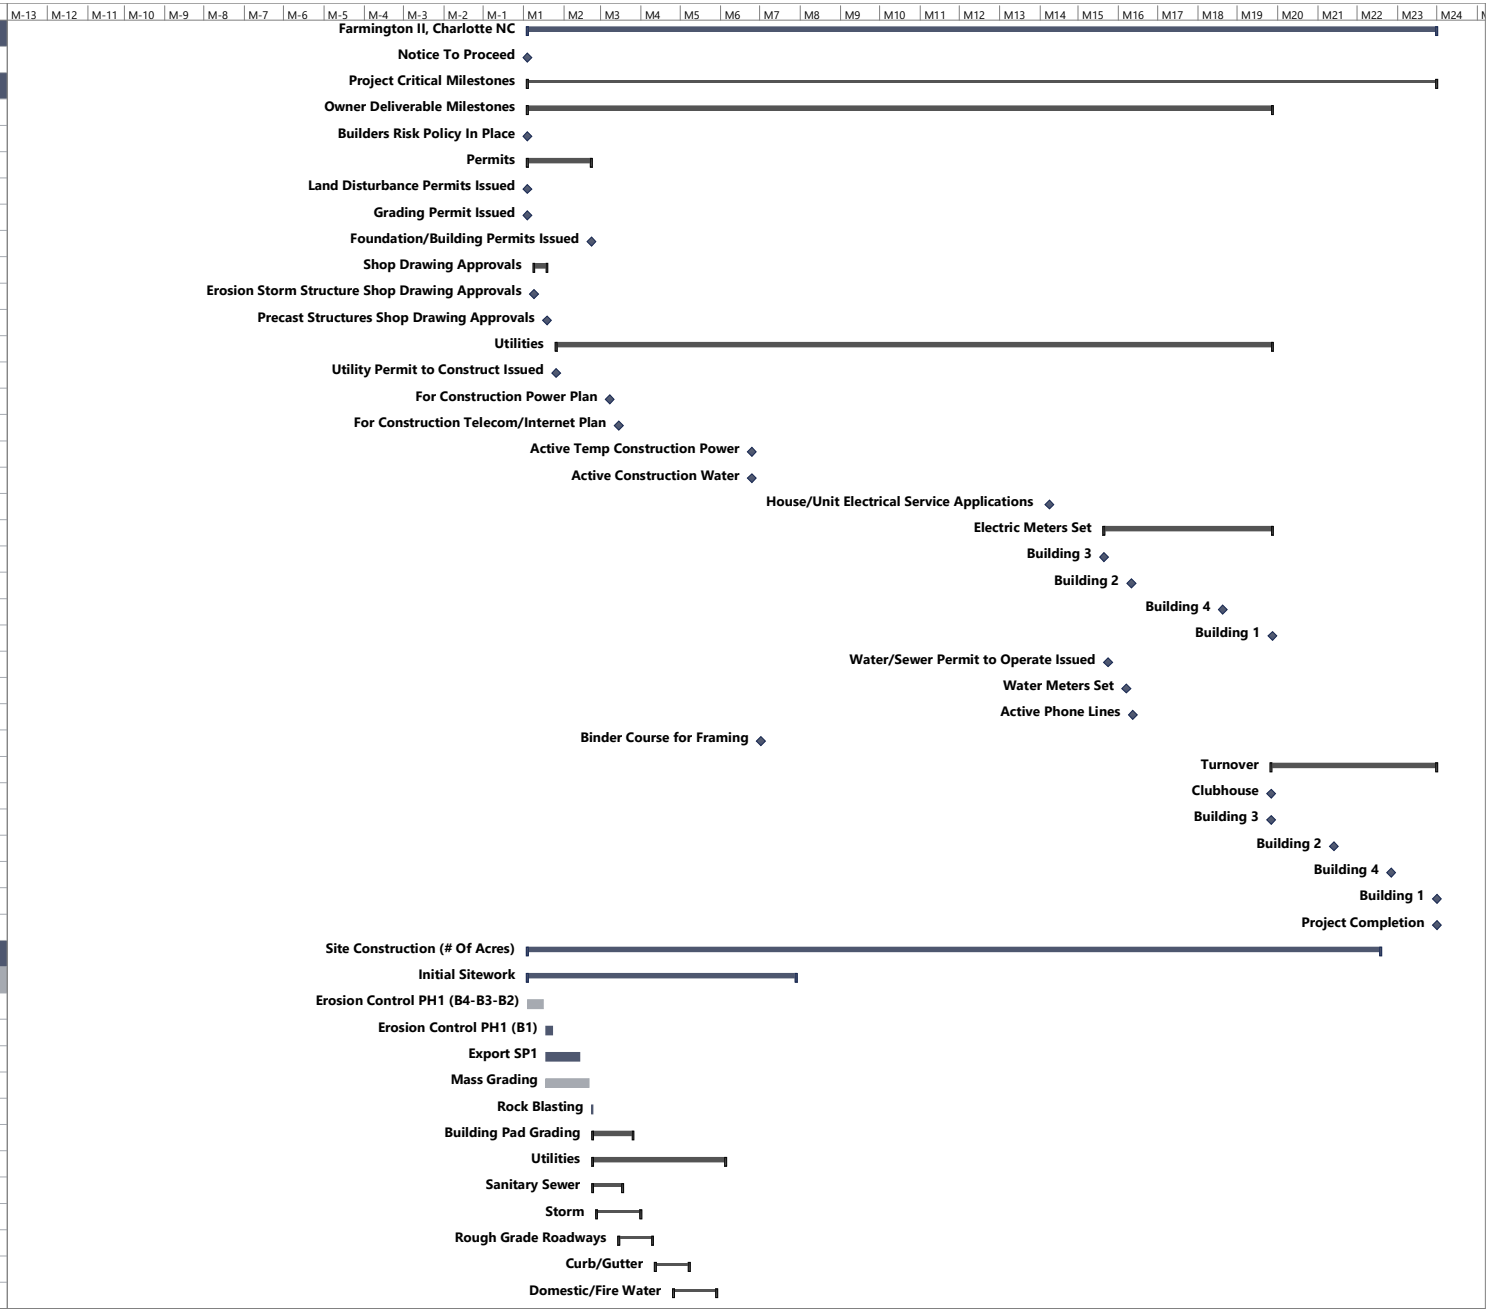


Exhibit E - Preliminary Construction Schedule

ID	Task Name	Duration
82	Primary/Secondary Conduit/Sleeving	20 days
87	Roadways/Parking Lots (Building 3,4,2)	34 days
92	Roadways/Parking Lots (Building 1)	24 days
97	Final Sitework	189 days
98	Phase 1 (Building 3, Pool)	105 days
103	Phase 2 (Building 2, Maint, Trash, Garage)	40 days
107	Phase 3 (Building 4, Garages)	50 days
111	Phase 4 (Building 1)	55 days
115	Vertical Construction (245 Units)	444 days
116	Building 3 (82 Units)	353 days
117	U/G Rough, Foundations, Slab, Podium	38 days
125	Stair Tower/Elevator CMU	15 days
126	Framing	115 days
143	Exteriors	89 days
165	Rough-In / Insulation	111 days
198	Interiors	103 days
274	Elevator	25 days
276	Inspections & Turnover	59 days
309	Building 3 Complete	0 days
310	Building 2 (73 Units)	349 days
311	Concrete and Undergrounds	52 days
321	Stair Tower/Elevator CMU	15 days
322	Framing	97 days
339	Exteriors	86 days
360	Rough In/Insulation	95 days
393	Interiors	116 days
469	Elevator	25 days
471	Inspections & Turnover	51 days
504	Building 2 Complete	0 days
505	Building 4 (78 Units)	329 days
506	Concrete and Undergrounds	51 days
516	Stair Tower/Elevator CMU	15 days
517	Framing	101 days
534	Exteriors	86 days
555	Rough-In / Insulation	88 days
588	Interiors	96 days
664	Elevator	25 days
666	Inspections & Turnover	45 days
699	Building 4 Complete	0 days
700	Building 1 (91 Units)	303 days
701	Concrete and Undergrounds	57 days
710	Stair Tower/Elevator CMU	15 days
711	Framing	98 days
728	Exteriors	104 days
749	Rough-In / Insulation	104 days
782	Interiors	98 days
859	Elevator	30 days
861	Inspections & Turnover	55 days
894	Building 1 Complete	0 days

